DOING AGILE

PRIORITISATION

Doing the Right Work & Doing the Work Right

Strategy

Mission & Vision

Objectives & Goals

Strategic Initiatives

Program

DISCOVERY SECTION

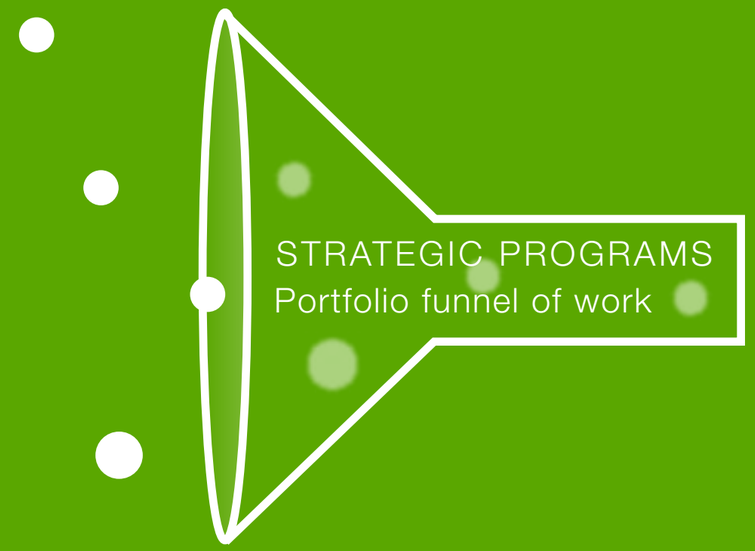

Doing the Right Work

DELIVERY SECTION

Doing the Work Right

Prioritisation

TEAM 1 1 2 3 4 5 6

TEAM 2 1 2 3 4 5 6

TEAM N 1 2 3 4 5 6

Slow Down in Order to do More

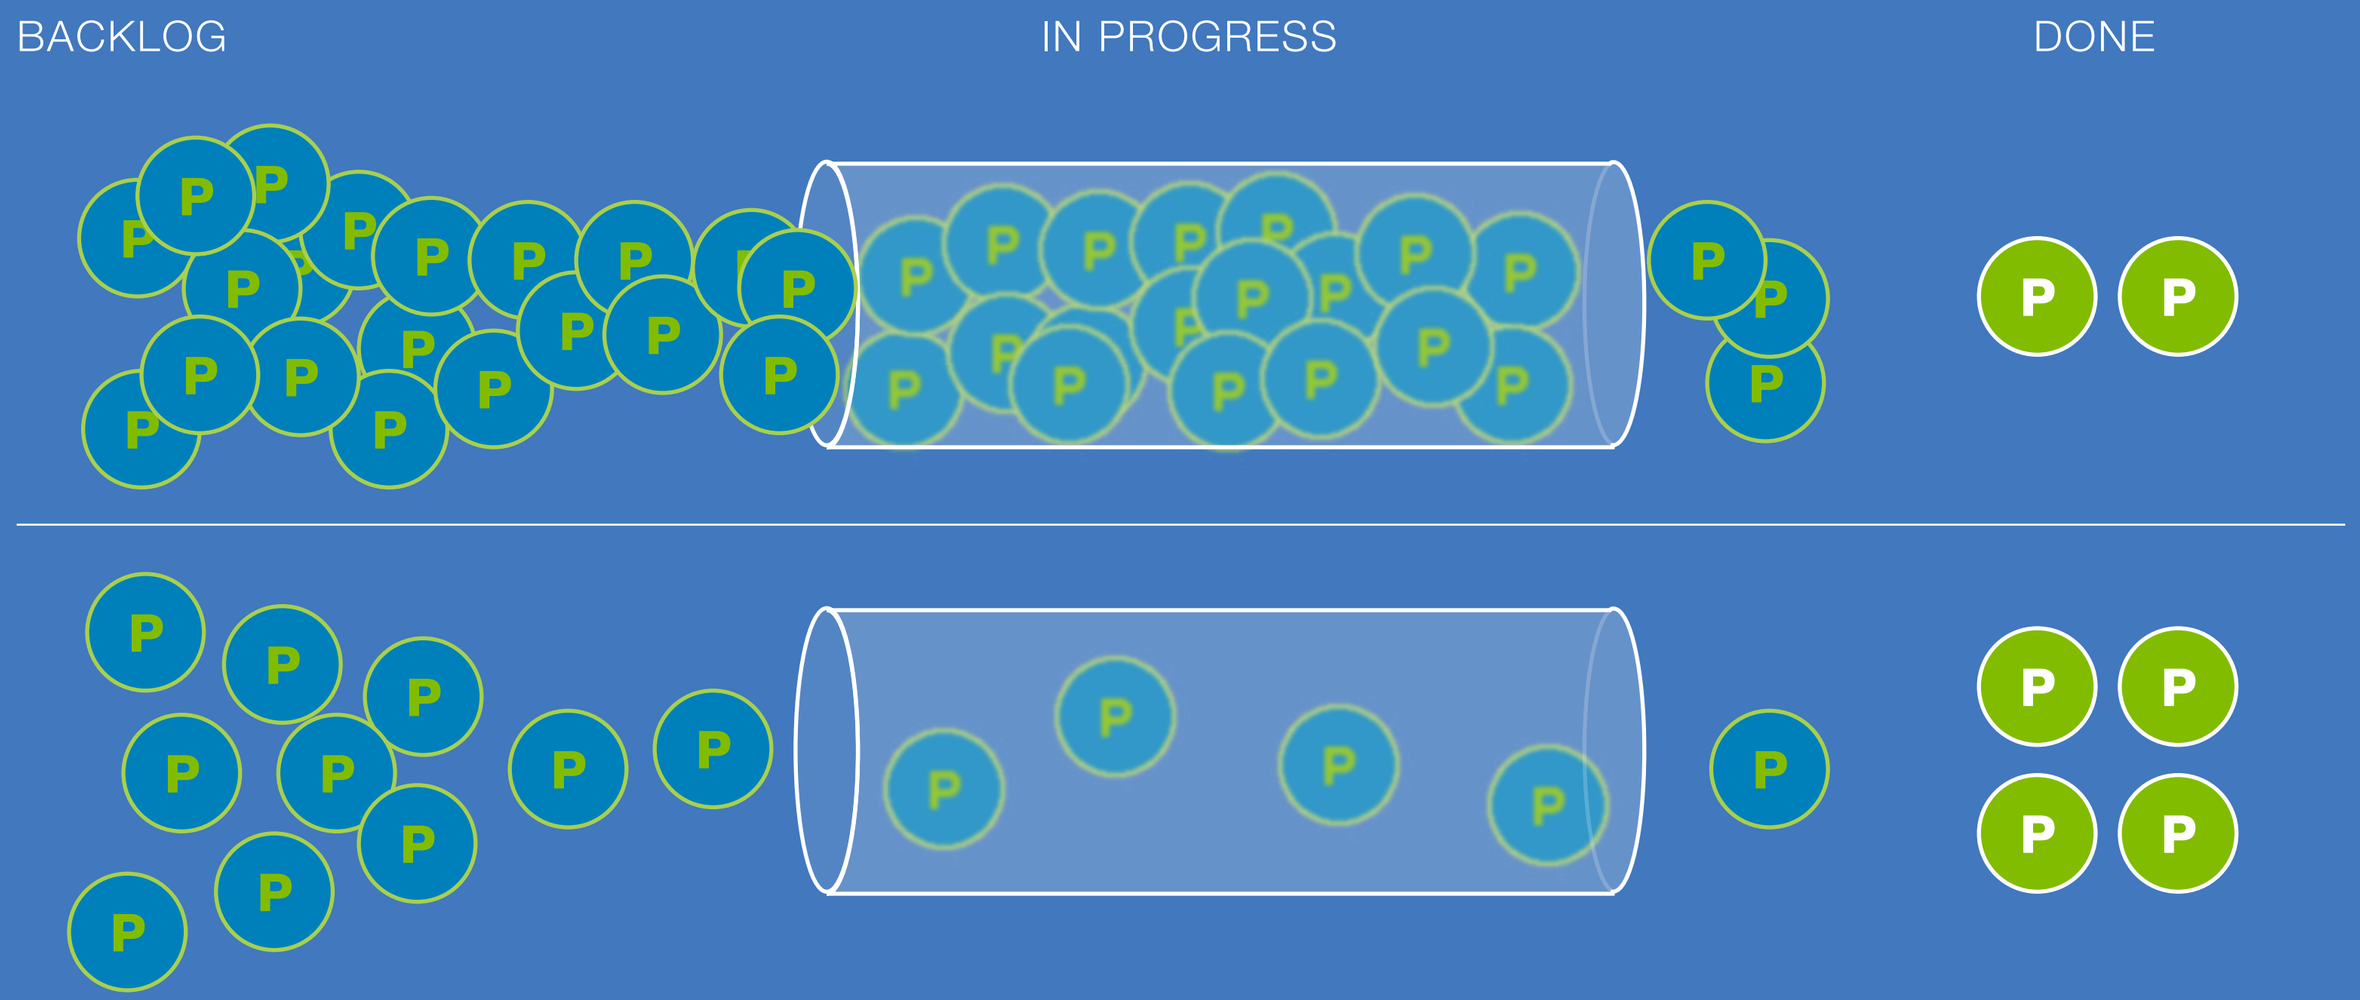

Minimize WIP by **Managing the Funnel**
and not Overburdening

Agile Project Characteristics

- Small cross functional teams (Incl. customer)
- Loosely coupled tightly aligned
- Iterative
- Highly collaborative
- Authentic transparency
- Pull work to WIP limit
- Self Organizing
- Flexible to change
- Facilitated and managed
- Disciplined approach
- Shared and consistent clarity of purpose
- Focused on feedback & continuous improvement

DOING AGILE

TEAM ROLES

Cross Functional Empowered Teams

CORE

5-9 People
Dedicated
Cross Functional
Empowered

Business SME (Customer)
Analysts
Developers
Testers
Solution Architect

IM

EXTENDED

Key Stakeholders
External experts
Enterprise Architect

PM

GOVERNANCE

Steering committee
PMO

Key Roles

- TM The Team (the doer's)
- PO The Product Owner
- IM The Iteration Manager
- PM The Project Manager
- CM Change Manager

These are the committed parties, the people responsible for the success of the project and product. There will be other involved parties, but they won't be responsible for the success of the project or product

Team Roles and Responsibilities

Key Roles and Responsibilities

Core

- **IM** — Iteration Manager
- **SME** — Subject Mater Expert
- **TM** — Team
- **PO** — Product Owner

Extended

- **PGM** — Program Manager
- **PM** — Project Manager
- **SH** — Stake Holder
- **CM** — Change Manager
- **EXP** — Experts

Steering

- **SC** — Steering Committee
- **SP** — Sponsor

Team Responsibilities

Self organization

Making commitments

Meeting commitments

Management of the team – every team member is responsible for this

Respecting other members of the team

Product Owner Responsibilities

PO

IM PM CM

Product Owner

- Voice of the customer/project sponsor
- Defines features of the product
- Responsible for the profitability of the product (ROI)
- Manages stakeholders and their interests
- Accepts/rejects work results
- Maintains just-enough, just-in-time feature detail
- Shares success with the team

Iteration Manager Responsibilities

Iteration Manager

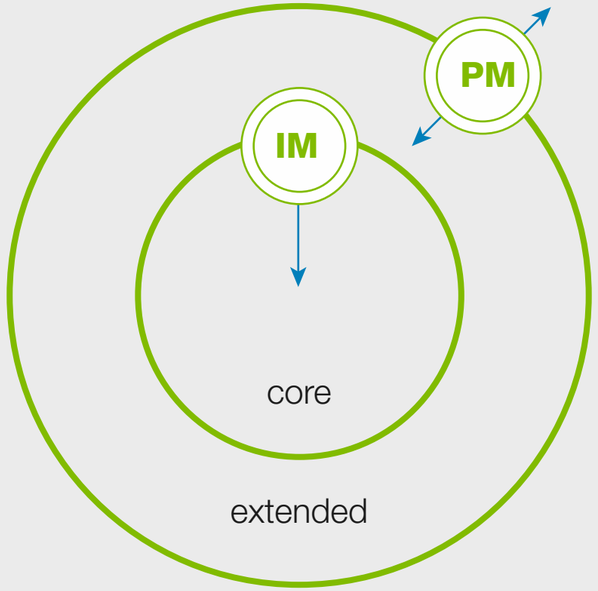

- Servant leadership/facilitation of the Core team – POD – during delivery and deployment
- Helps remove impediments
- Acts as guardian of the iteration process/framework
- Improves lives of team members by facilitating empowerment and creativity
- Helps team improve productivity in any way possible
- Works with team and PO to ensure each iteration of the product is potentially shippable
- Works with team and PO to ensure quality is never compromised
- Coaches and helps team members in the Agile way of working
- Energize and inspire the team

Project Manager Responsibilities

PM

PO IM CM

Project Manager

- Facilitates and manages the Discovery phases and cycles
- Serve as leadership/facilitation of the Project (multiple Pods)
- Facilitates dependency management using the ‘Team of Teams’ model across Projects and Pods and
- Helps remove impediments
- Acts as guardian of the overall project process/framework
- Improves lives of team members by facilitating empowerment and creativity
- Helps team improve productivity in any way possible
- Helps the PO with multi-stakeholder management
- Manages and communicates with non PO stakeholders
- Works with team and PO to ensure quality is never compromised
- Coaches and mentors the Agile way of working
- Energizes and inspires the team to greater heights

Change Manager Responsibilities

- Facilitates and manages the roll out and implementation of the project outcomes.
- Leads the Change Management Pod (sometimes called ‘Coms and Change’
- Looks after end user comms, training, process changes and overall adoption
- Closely involved in end user testing and acceptance
- Works closely with all the other IMs
- Works Agile

DOING AGILE

DISCOVERY

The Program Pattern used to launch and execute programs

Strategy

IDEA

Strategic Initiative
New Requirement
Enhancement
Problem
Opportunity

DISCOVER

Understand & Strategize

Governance /
Funding Gates

DELIVER

Iteratively build,
test & deliver

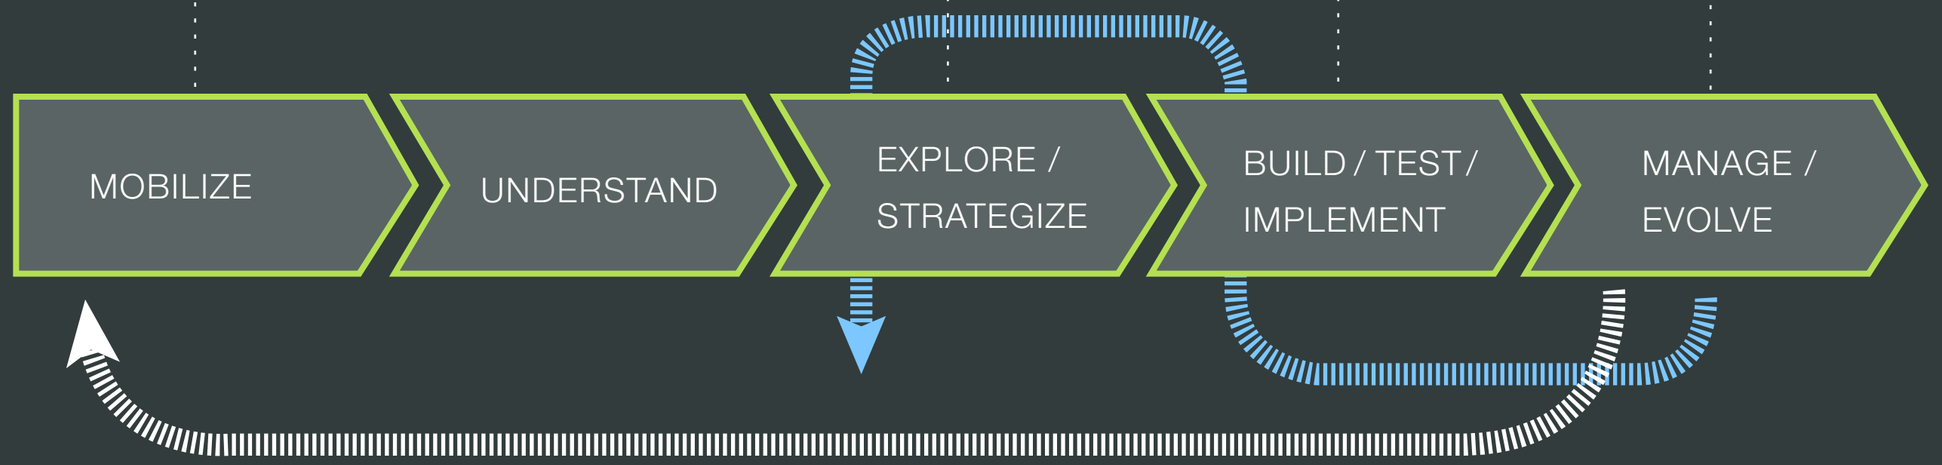

Defining the Desired Outcome & Benefits

Business Outcomes

Estimated Benefits

Each business outcome must have one or more estimated $$ value benefits

SMART Requirements

S pecific

A requirement must say **exactly what is required.** There is no ambiguity; consistent terminology; simple - avoid double requirements i.e. X and Y; appropriate level of detail

M easurable

Measureable when at all possible. Once the system/process has been constructed, it **can be verified** that this requirement has been met.

A ttainable

Physically possible for the system/process to exhibit that requirement under the given conditions. The consequence of unattainable requirements is that the system will never be accepted or prohibitively expensive or both

R ealisable

Possible to achieve this requirement given what is known about the constraints under which the project must be developed.

T raceable

Traceabiilty is the **ability to trac**e (forwards and backwards) a requirement from its conception through its completion/deployment

SMART Goals

Each objective should have one or more SMART goals

(Specific: Measureable, Actionable, Realistic, Time bound)

AGILE AT WORK

DELIVERY

Setting up for Success

1 THE WORK

Approved project scope

2 RESOURCING

The team

The PM & IM

The Customer – Product

Owner

$$ - Budgets

Facility – space

The Lifecycle of Delivery

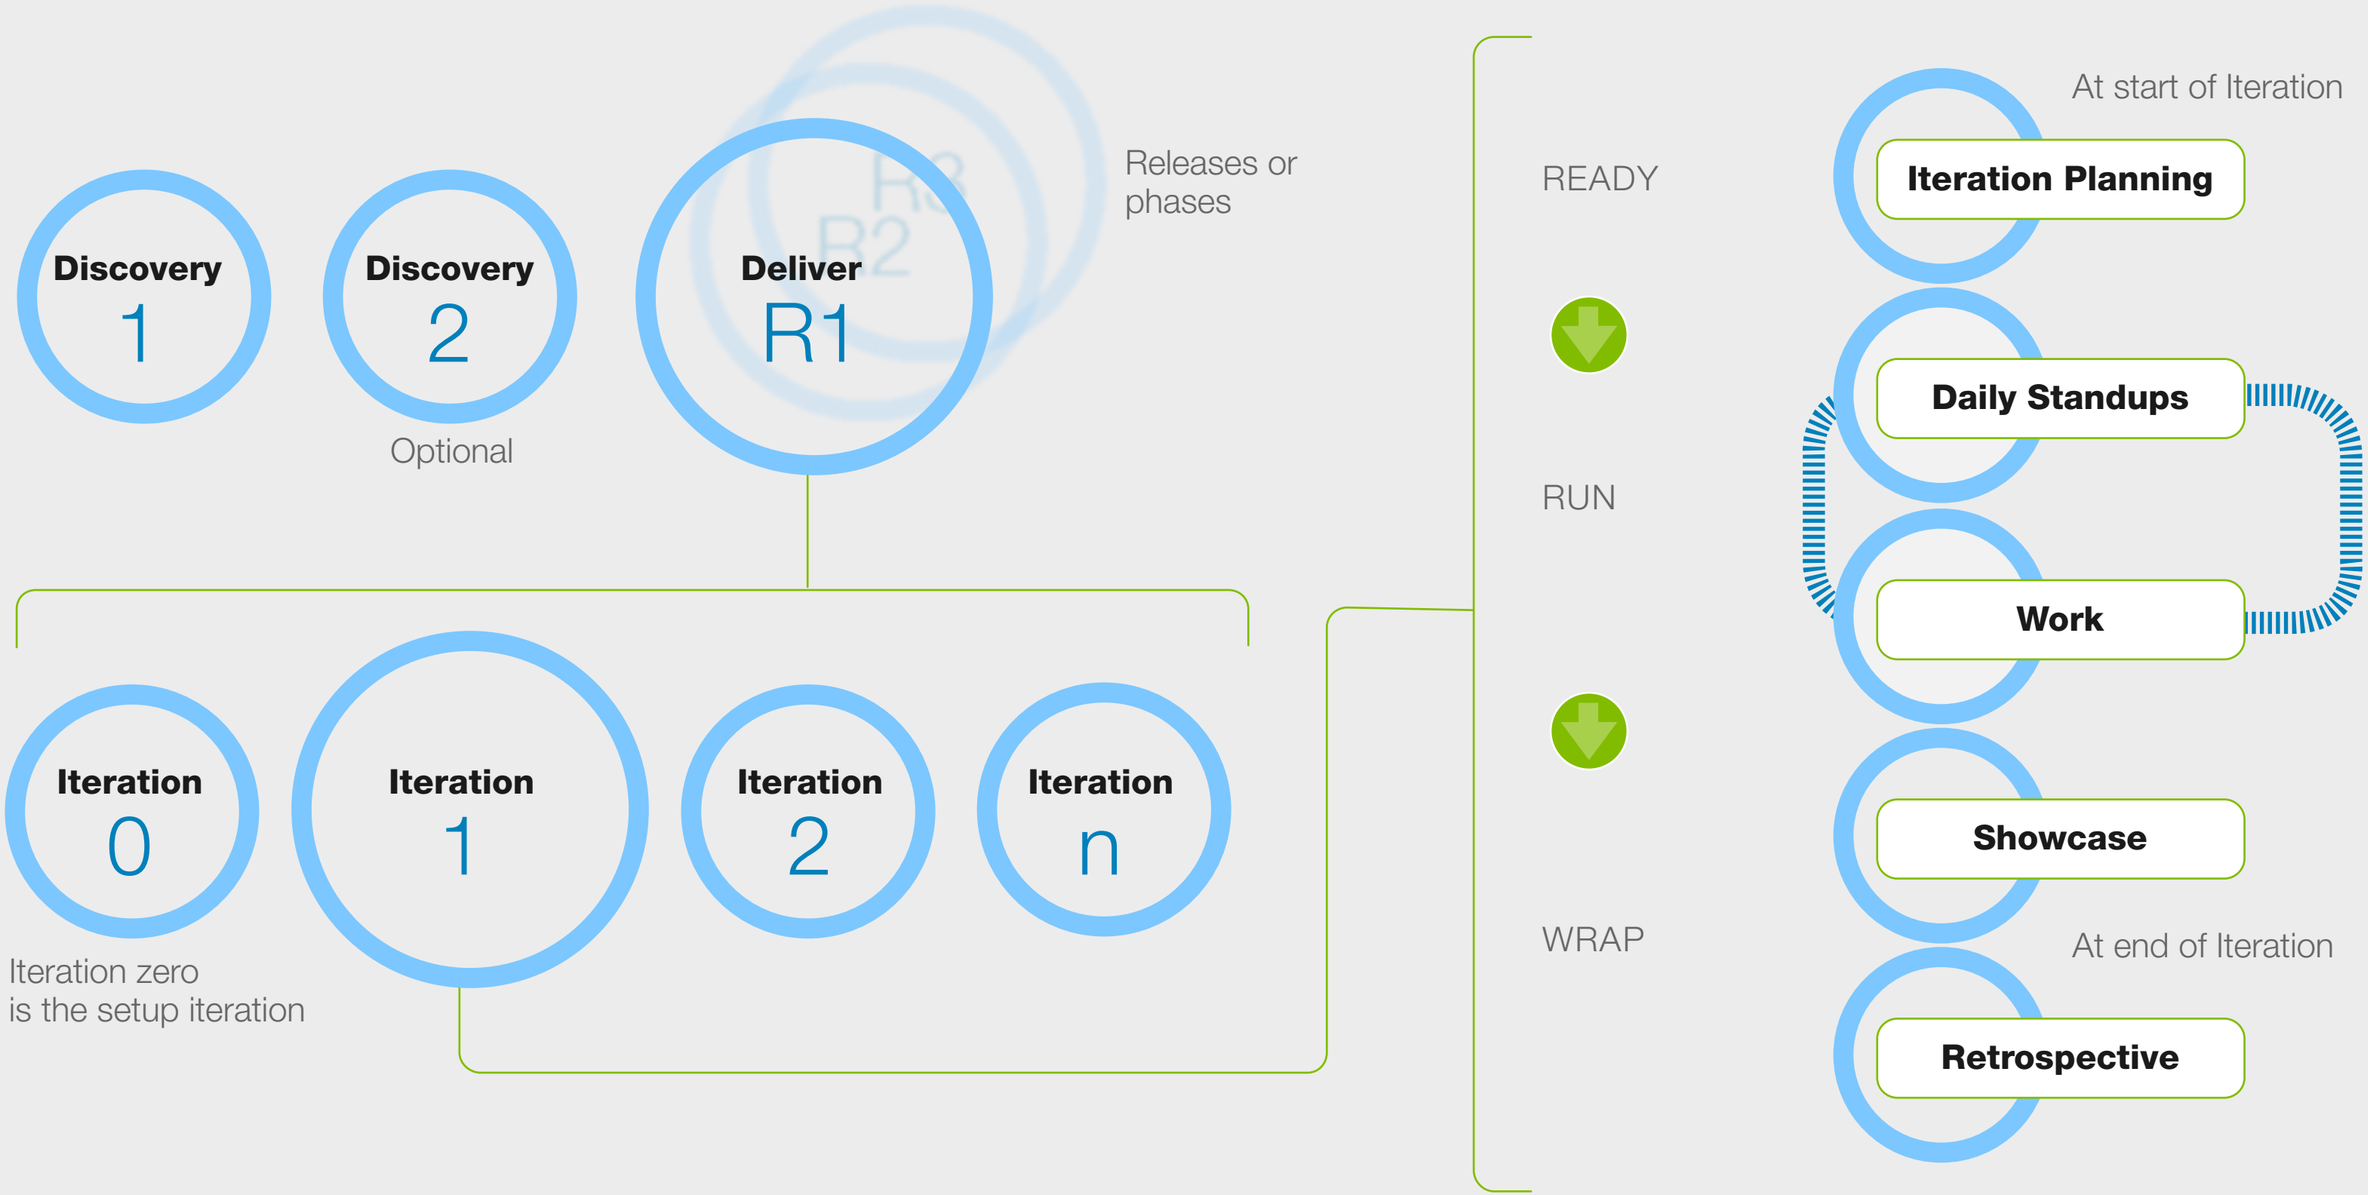

Scrum

Inputs from customers, team, managers, execs

Product Owner

Product Backlog

A Prioritized List

of what is required: features, bugs to fix

Team

Sprint Planning Meeting

The team commits to as much high priority backlog as can be completed by the end of the sprint

Sprint Backlog

Task Breakout

1-4 Week Sprint

Sprint end date and deliverable do not change

Scrum Master

Daily Standup Meeting

15-30 Minutes

Sprint Review

Finished Product

Product Increment

Sprint Retrospective

AGILE AT WORK

STORIES

The Life of a Story

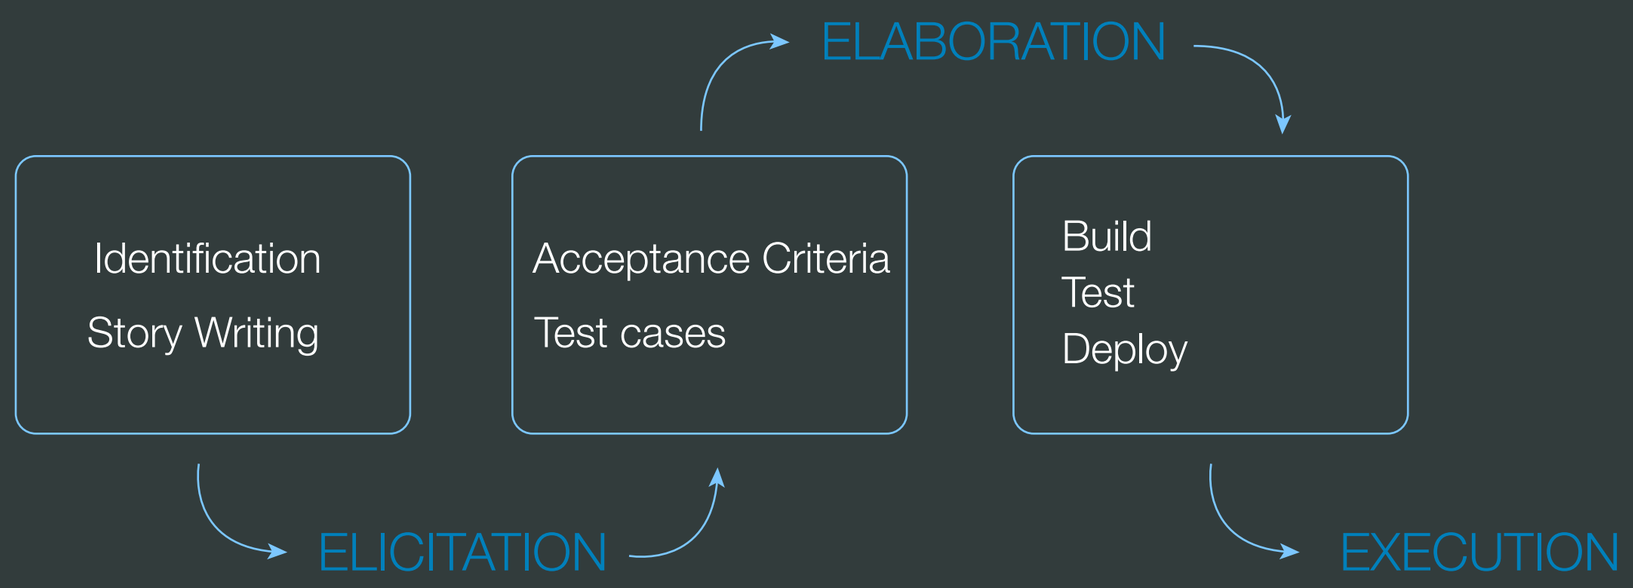

Prioritization | **Estimation** | **Planning**

Story Identification

Personas

Process

Outcomes

Feature breakdown

Design Thinking Practices

Business Canvas

Value Stream Mapping (as-is and to-be)

Brainstorming

User/customer interviews

Story Elaboration

ALWAYS	SOMETIMES	LESS OFTEN
ID	Narrative	Technical Design
Title	Lo-fi Prototype	Data Model
Acceptance Criteria	Assumptions	Link to High Level Scenarios
Relative Size Estimate	Constraints	GUI Design

Collaborate to Elaborate

Story Writing

Who — **Personas**

What — **Process**

Why — **Outcomes**

As a _____

I want _____

So that _____

AGILE AT WORK

RELEASE PLANNING

Iteration 1

5th → **16th**
November

- Prioritise features and stories
- Estimate features and stories
- Estimate velocity
- Fill the iteration buckets
- Cater for contingency
- Set up the release wall

Total = x

Iteration 2

19th → **30th**
November

- Prioritise features and stories
- Estimate features and stories
- Estimate velocity
- Fill the iteration buckets
- Cater for contingency
- Set up the release wall

Total = x

Iteration 3

3rd → **14th**
December

- Prioritise features and stories
- Estimate features and stories
- Estimate velocity
- Fill the iteration buckets
- Cater for contingency
- Set up the release wall

Total = x

Product Backlog

On the wall and in a tool

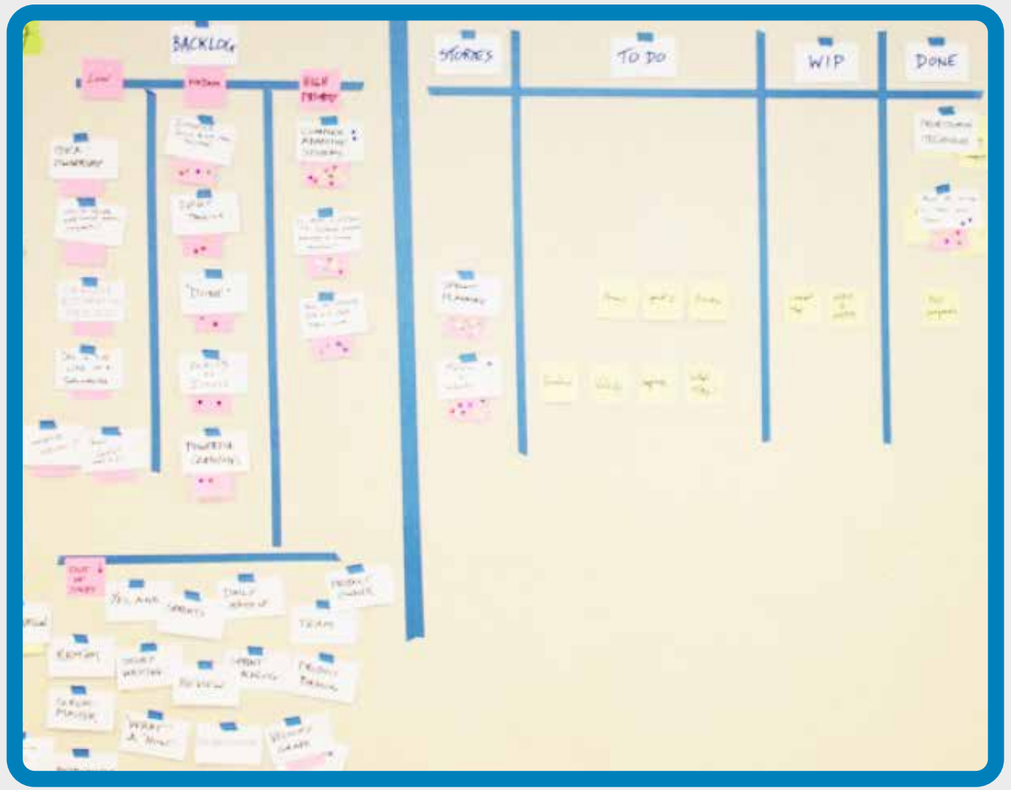

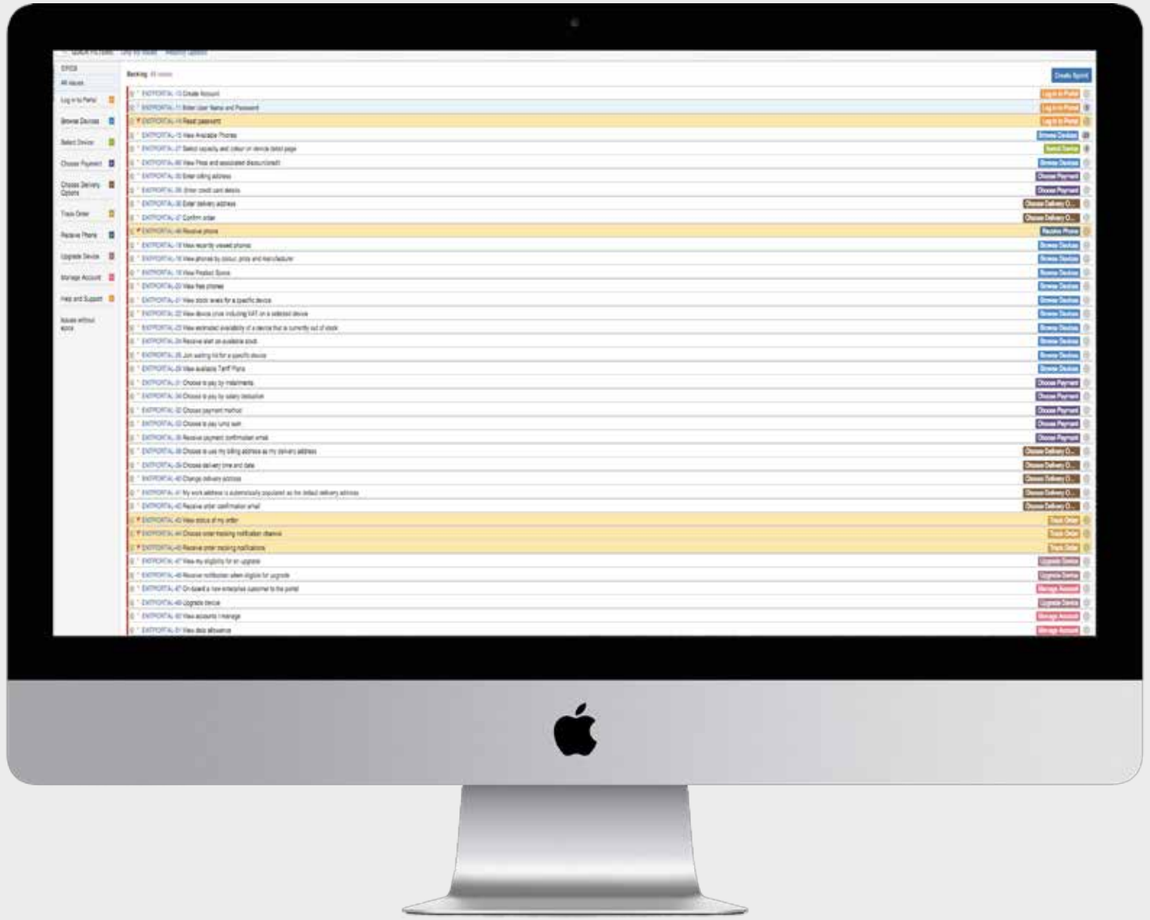

Velocity

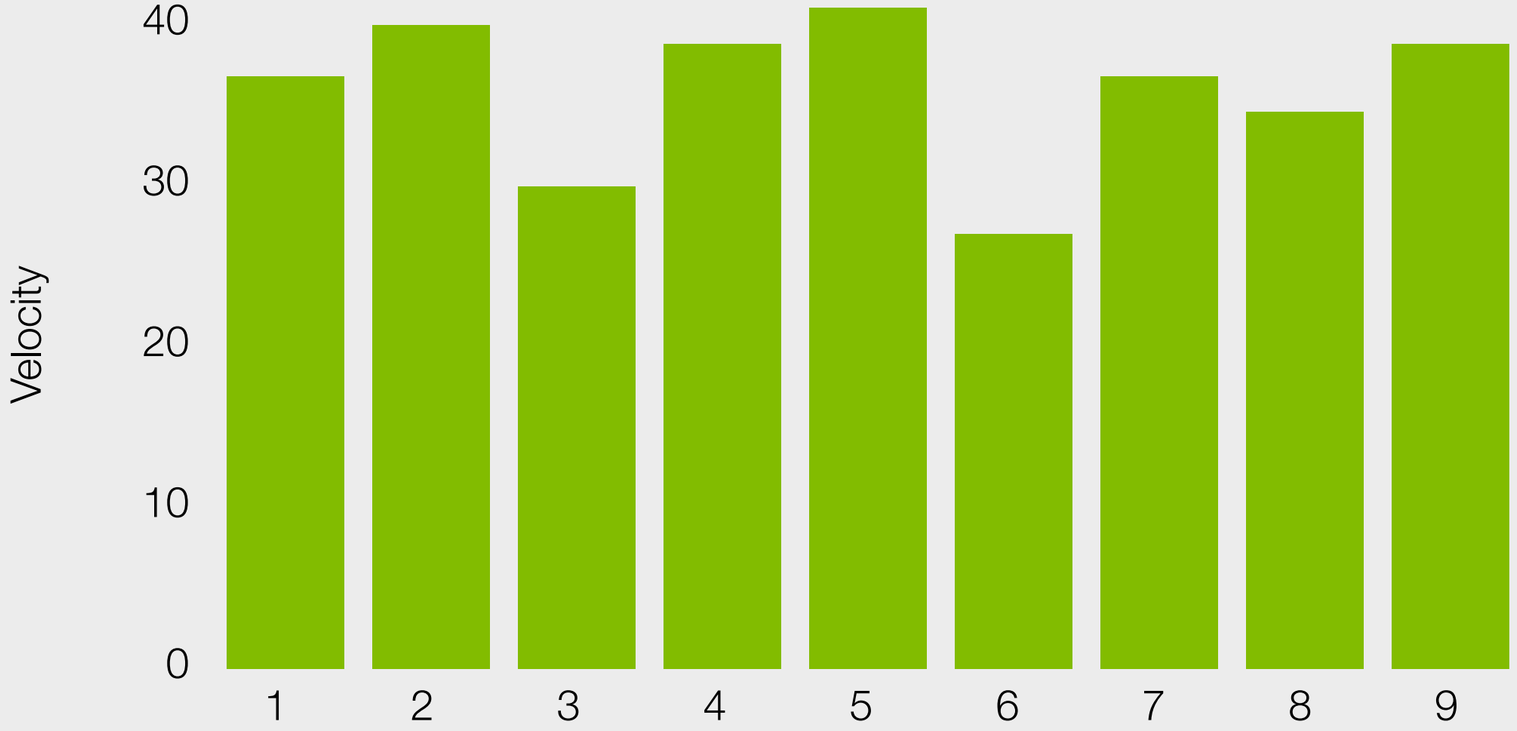

A useful long-term measure of the amount of work completed per iteration.

Most useful over at least a handful of iterations.

Velocity is measured in the units you use to estimate product backlog items.

Estimate Size; Derive Duration

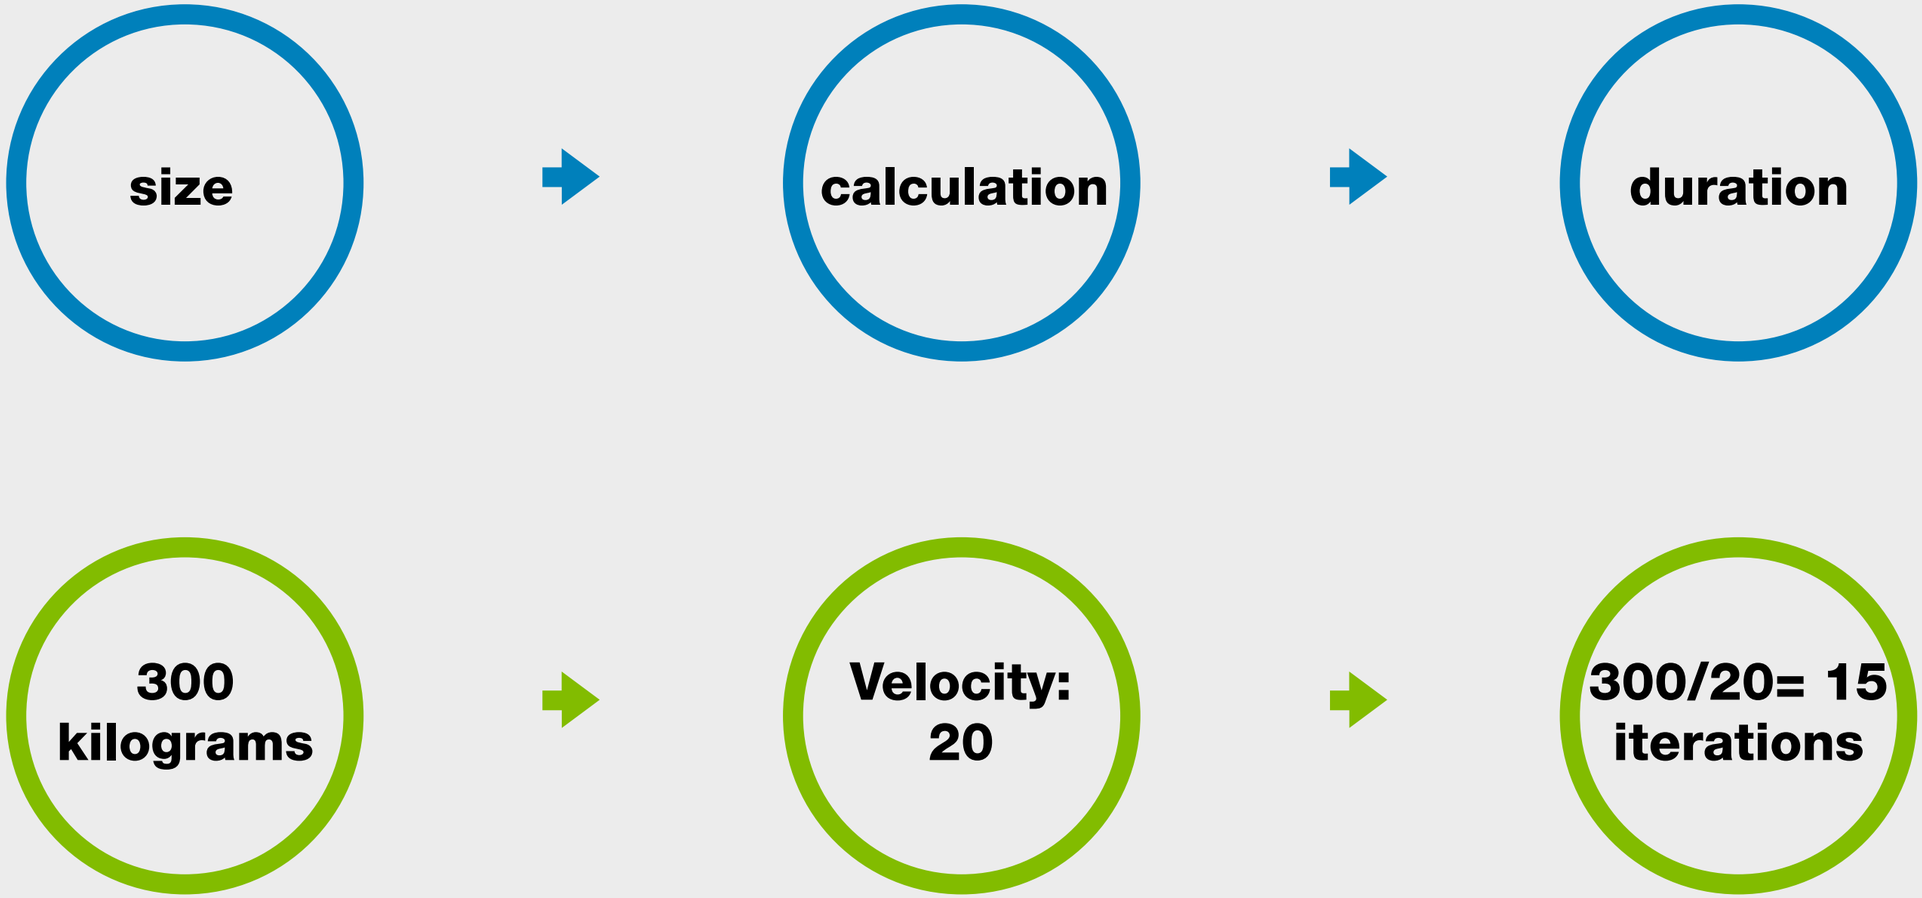

Release Plan

Release Wall

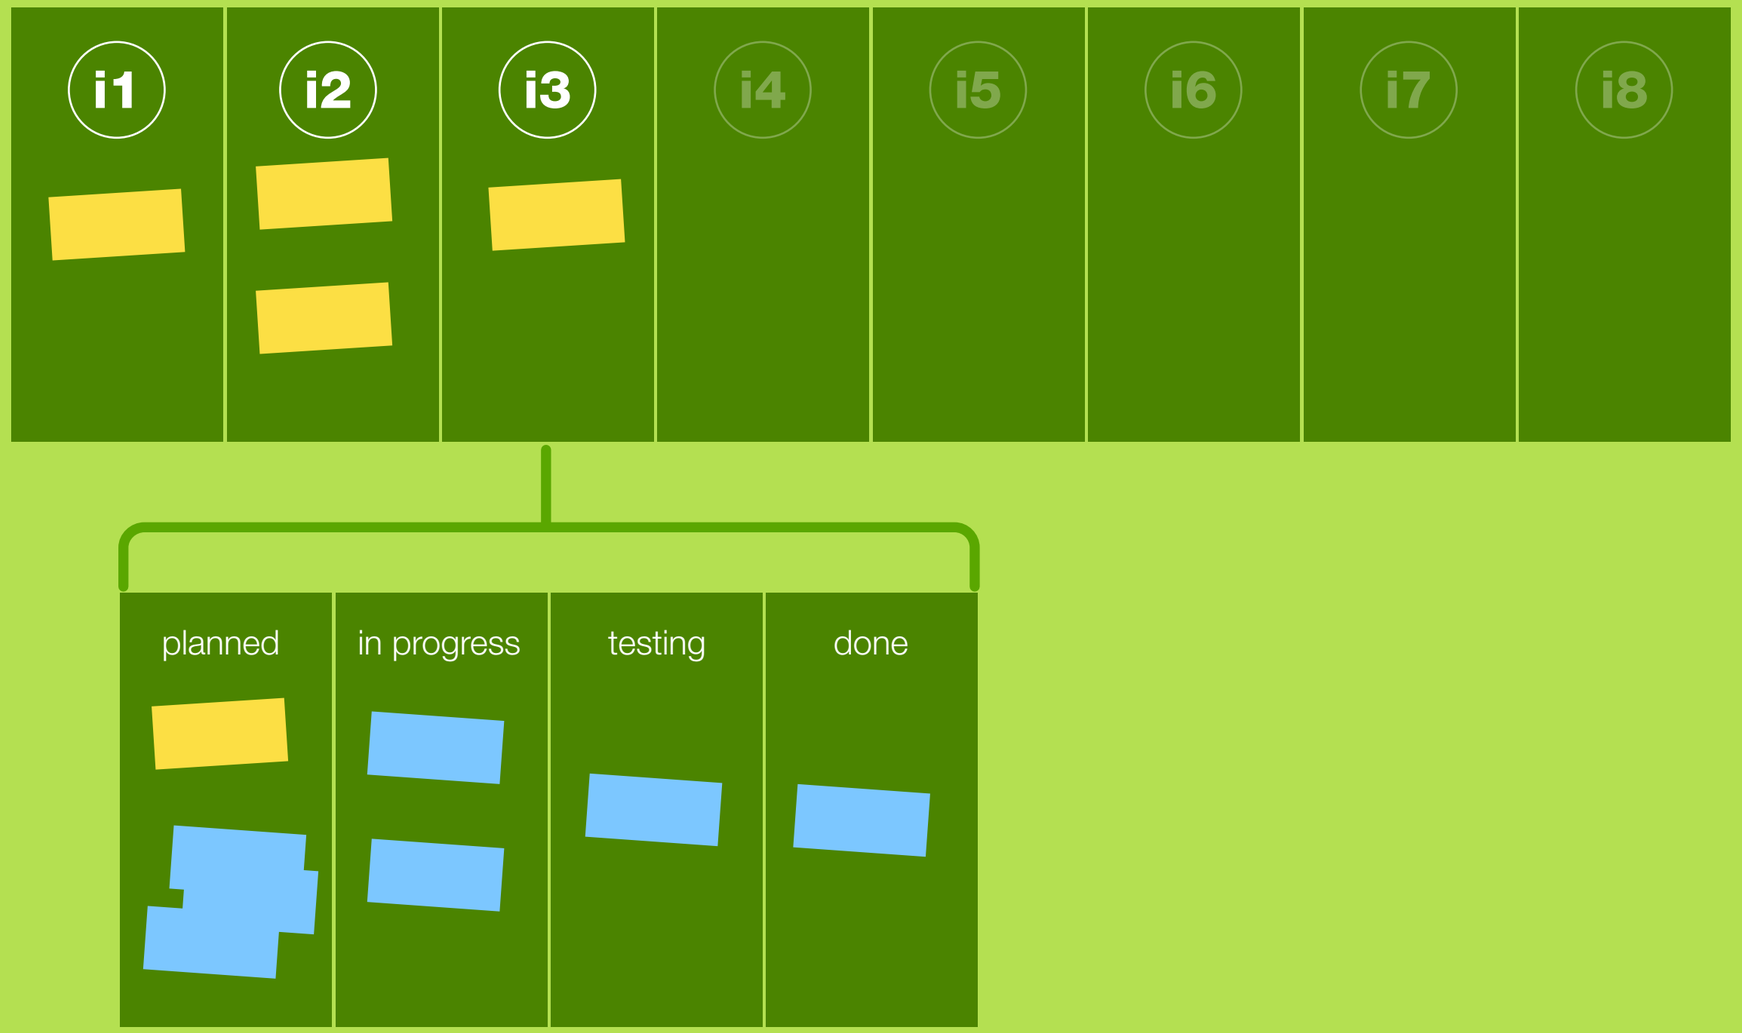

Iteration Wall
